
Cargo Inspection Checklist

Transport & Logistics

INTERIOR OF THE CONTAINER

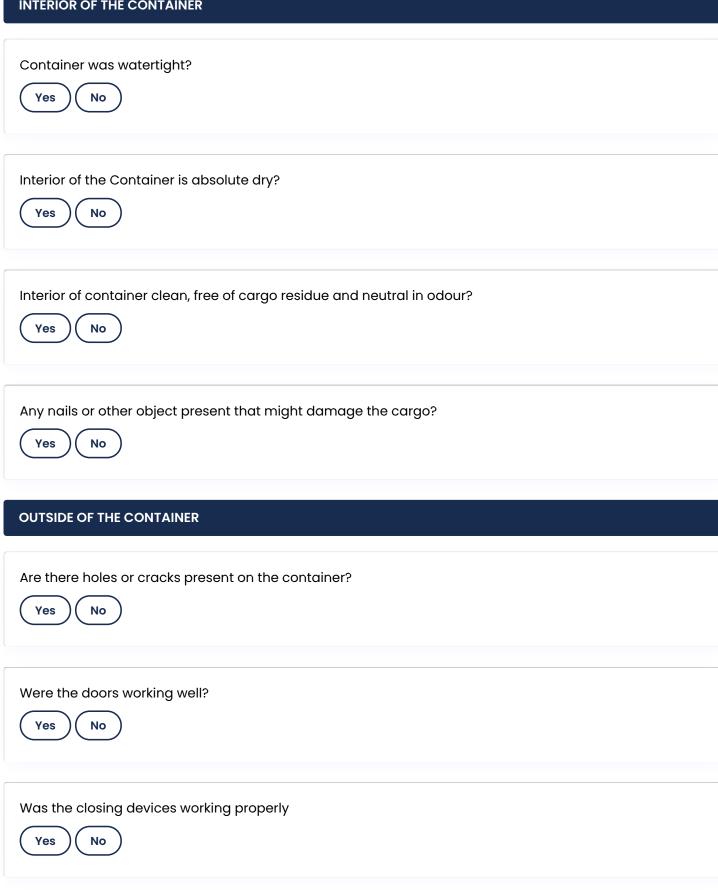

| FOST FACRING CHECKS |
|--|
| Is the container well packed for the cargo and anticipated transit stresses? Yes No |
| Copy of the packing placed in a visible manner? Yes No |
| Lumber used as a packaging material? Yes No |
| Are the roof covering and doors closed properly? Yes No |
| Closures secured wit metal or other seals to reduce theft risk? Yes No |
| Previous adhesive labels removed? Yes No |
| PRE LOADING |
| Select the type of holds Single Deck Steel Pontoons |
| Select the type of hatch covers Steel Folding Steel Pontoons |

| REQUIRED SHIPPING DOCUMENTS |
|---|
| Was the proforma invoice complete or incomplete? Complete Incomplete |
| Was the commercial invoice complete or incomplete? Complete Incomplete |
| Was the packing list complete or incomplete? Complete Incomplete |
| Was the certificates of origin complete or incomplete? Complete Incomplete |
| Was the shipper's letter of Instruction complete or incomplete? Complete Incomplete |
| Was the bills of lading complete or incomplete? Complete Incomplete |
| Was the dangerous goods form completed? Complete Incomplete |
| Select the type of container 20' dry frreight 20' flat rack 20' open top 20' tanker 40' opn top 40' platform 40' reefer 40'collapsibleflatrack 40'Dry Freight 40'flat rack 40'high cube reefer 45' High cube dry |

| Type of Cargo? |
|---|
| textarea |
| |
| SIGN OFF |
| Mark if the following were checked prior to loading Availability of Stevedores Platform Bilges Empty Compression Bars Draining Canals/Holes/Pipes Electric Circuits/Lights in the Holds Turned Off Entrance Hatches/Ladders Hatch Coaming Heat Sources (lights, engines/pipelines, etc.) Hold Ventilation Closed Rubber gaskets Tightness of Moveable Bulkhead Trimming Holes on Hatch Covers Ultrasound Leak Detector Test Wedges/Cleats |
| Comment if there was an additional observations textarea |
| Please provide Inspectors Name |
| Inspectors Signature SIGNATURE |
